

WARNING: THIS IS NOT A SURVEY

Parcel Information

Parcel Number:	H500000208	Township:	Mocksville
NCPIN Number:	5739865013	Municipality:	
Account Number:	2318500	Census Tract:	37059-806
Listed Owner 1:	ANGELL ROBERT MICHAEL	Voting Precinct:	NORTH MOCKSVILLE COUNTY
Mailing Address 1:	219 FARMLAND ROAD	Planning Jurisdiction:	Davie County
City:	MOCKSVILLE	Zoning Class:	DAVIE COUNTY R-A
State:	NC	Zoning Overlay:	DAVIE COUNTY QD
Zip Code:	27028-4163	Voluntary Ag. District:	No
Legal Description:	LOT 9 FARMLAND ACRES SECTION TWO	Fire Response District:	MOCKSVILLE
Assessed Acreage:	4.32	Elementary School Zone:	MOCKSVILLE
Deed Date:	4/1982	Middle School Zone:	SOUTH DAVIE
Deed Book / Page:	001160237	Soil Types:	GnB2,GnC2,ChA
Plat Book:	0005	Flood Zone:	
Plat Page:	041	Watershed Overlay:	DAVIE COUNTY
Building Value:		Outbuilding & Extra Features Value:	
Land Value:		Total Market Value:	
Total Assessed Value:			



**Davie County,
NC**

All data is provided as is without warranty or guarantee of any kind either expressed or implied including but not limited to the implied warranties of merchantability or fitness for a particular use. All users of Davie County's GIS website shall hold harmless the County of Davie, North Carolina, its agents, consultants, contractors or employees from any and all claims or causes of action due to or arising out of the use or inability to use the GIS data provided by this website.

6:00

DAVIE COUNTY HEALTH DEPARTMENT IMPROVEMENTS PERMIT AND CERTIFICATE OF COMPLETION

*Note: Issued in Compliance with G.S. of North Carolina Chapter 130—Article 13c.

Permit Number
2821

Name Mike Ansell Date 3-12-82

Location off Country Lane

Subdivision Name Farmhand Acres Lot No. 9 Sec. or Block No. _____

Lot Size Acres House Mobile Home _____ Business _____ Speculation _____

No. Bedrooms 3 No. Baths 2 1/2 No. in Family 4

Garbage Disposal YES NO

Auto Dish Washer YES NO


Auto Wash Machine YES NO

Type Water Supply County

Specifications for System: 900 Gallon Tank
Dirt Box - 300' X 3' X 12" Rock
System no deeper than 2.5' below
Present grade.

*This permit Void if sewage system described below is not installed within 36 months from date of issue.

3.12.82 -
To complete
design of the house
and complete started
with Kenneth Lewis 3/10/82
(System 200')

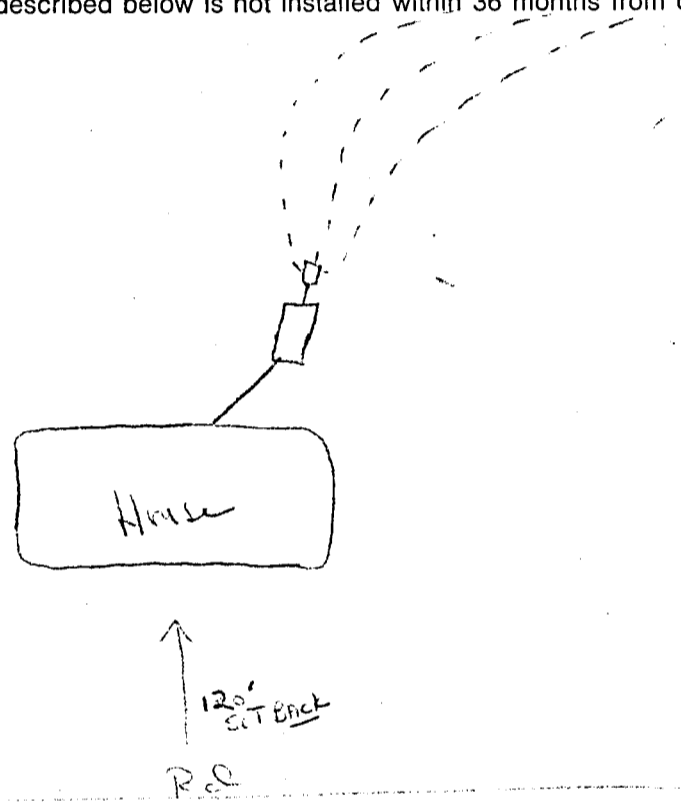


Improvements permit by J. Mando

*Contact a representative of the Davie County Health Department for final inspection of this system between 8:30-9:30 A.M. or 1:00-1:30 P.M. on day of completion. Telephone Number: 704-634-5985.

Final Installation Diagram:

System Installed by Dillard & Farto

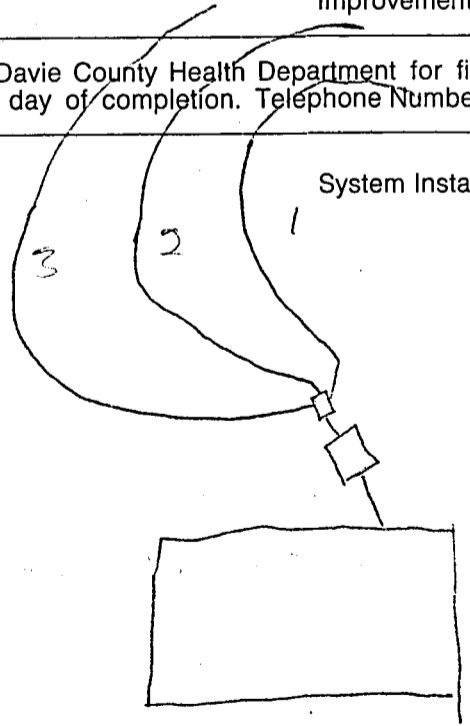

1-100 X 3 X 12" - level
2-100 X 5 X 12" - 1" fall
3-100 X 5 X 12" - 1" fall
Good workmanship!

Certificate of Completion Dall Date 2/12/82

*The signing of this certificate shall indicate that the system described above has been installed in compliance with the standards set forth in the above regulation, but shall in NO way be taken as a guarantee that the system will function satisfactorily for any given period of time.
